

SAFETY IMPROVEMENTS ON NEW JERSEY AVENUE NW

DC CONTRACT NO. DCKA-2018-C-0017

FAP No.: CM-2017(042)

CONSTRUCTION MANAGER'S WEEKLY PROGRESS REPORT 10

07/14/2019 – 07/20/2019

Project Website: www.newjerseyaverehab.com



07/15/2019- Trench Excavation for 6" DIP water line at/near 3rd St. and M St. NW.

1. EXECUTIVE SUMMARY

Project Description:

Work under this contract consists of safety/streetscape improvements along New Jersey Avenue, NW from N Street NW to H Street NW and the reconstruction New York Avenue, NW from First Street NW to 4th Street NW. The work includes but is not limited to the following items: Installation of new curb, gutter, and sidewalk; Installation of full depth pavement, Pavement resurfacing; Installation of utilities; Installation of flexible pavement; Installation of street light poles; Installation of traffic signals; Installation of signing and pavement markings; Installation of electrical duct bank; Relocation of over-height detection system; Installation of wireless vehicle detection system; Installation of landscape improvements; Installation of erosion and sediment control; Implementation of transportation management plan; Mobilization and demobilization, provision and maintenance of work and storage areas, Engineer's field facilities and performance of employee training; Removal and disposal of any material as a result of the activities listed above, unless stated otherwise in the contract drawings.

This project is 83.15% Federally Funded and 16.85% District-Funded. DDOT selected Capitol Paving of DC, Inc. (CPDC) as the contractor and awarded the \$12,055,691.00 contract on January 9, 2019. DDOT issued notice to proceed with contract work to CPDC with work to begin on 05/13/2019 and a substantial completion date of 11/23/2020.

2. WORK PROGRESS

The following work was performed during this period:

- Furnished and installed ductile iron pipe, valves, and valve casings for the waterline at the intersection of 3rd St NW and M St NW. Backfilled trench and placed and compacted temporary asphalt.
- Relocated traffic signal poles onto temporary bases near the intersections of New York Ave NW and M St NW.
- Installed schedule 40 PVC conduit for electrical duct bank on 2nd St NW between H St NW and I St NW.
- Installed electrical manholes at the intersection of K St NW and New Jersey Ave NW.
- Furnished and installed ductile iron pipe, valves, and valve casings for the waterline at the intersection of New Jersey Ave NW and N St NW. Backfilled trench and placed and compacted temporary asphalt.
- Relocated traffic signal poles onto temporary bases near the intersections of New Jersey Ave NW and K St NW.


3. PHOTOS OF WORK PERFORMED THIS PERIOD



07/16/2019 – Installing PVC pipes for electrical duct bank between MH-16 & L-44.



07/16/2019 – Excavation to set up MH-A at SE corner of NJ & K St. NW.

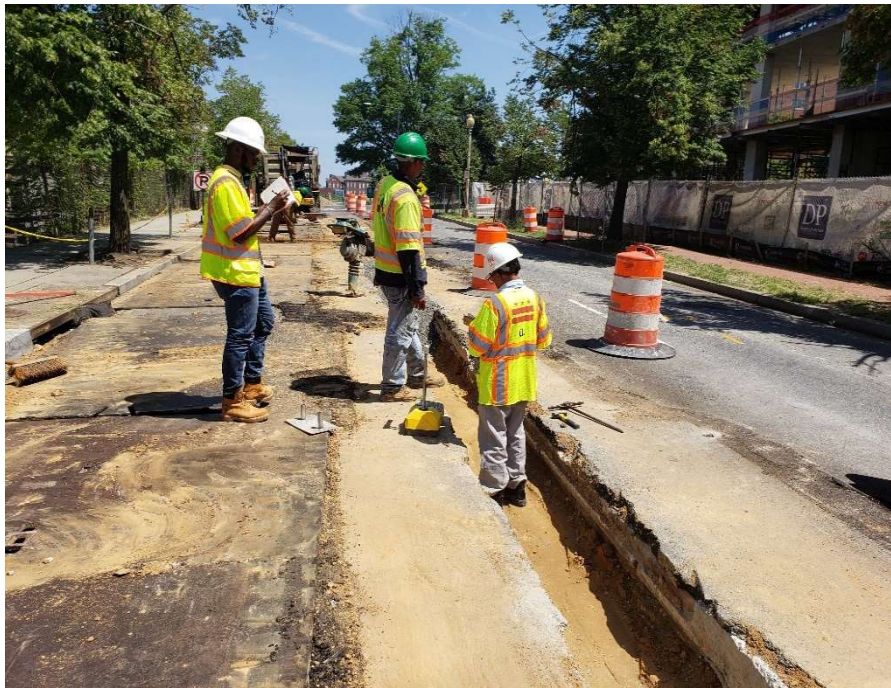

07/17/2019 – Moisture-Density Test for Soil backfill between MH-15 & MH-16



07/18/2019 – Trench Excavation for 8" DIP at Intersection of 3rd St. & M St. NW.



07/18/2019 – Temporary Asphalt Placement at N & New Jersey Ave. NW.



07/17/2019 – Soil backfill for MH-B at NW Corner of K St. & New Jersey Ave. NW



07/16/2019 – 8" DIP water line installation at SW corner of NJ Ave. & N St. NW



07/16/2019 – Relocate Traffic Light Poles at NW corner of NY Ave. & M St. NW



07/15/2019 – Installing Gate Valve at/near 3rd St & M St. NW (Crossing 3rd St. NW)



07/16/2019 –Temporary Asphalt Placement/compaction at 3rd St. & M St. NW.
