

## SAFETY IMPROVEMENTS ON NEW JERSEY AVENUE NW


DC CONTRACT NO. DCKA-2018-C-0017

FAP No.: CM-2017(042)

# CONSTRUCTION MANAGER'S WEEKLY PROGRESS REPORT 79

11/08/2020 – 11/14/2020

Project Website: [www.newjerseyaverehab.com](http://www.newjerseyaverehab.com)

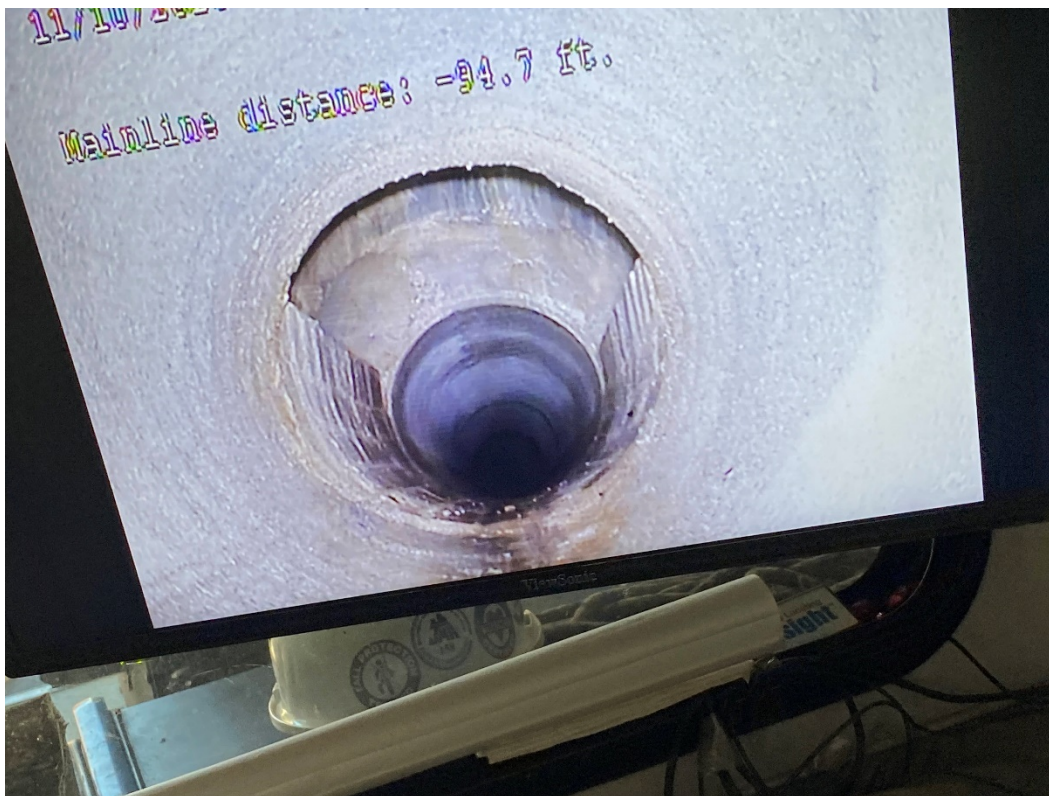

11/09/2020 – CCTV inspection for sewers pipeline along NJ Ave between N St. and K St.

## 1. EXECUTIVE SUMMARY

### Project Description:

Work under this contract consists of safety/streetscape improvements along New Jersey Avenue, NW from N Street NW to H Street NW and the reconstruction New York Avenue, NW from First Street NW to 4th Street NW. The work includes but is not limited to the following items: Installation of new curb, gutter, and sidewalk; Installation of full depth pavement, Pavement resurfacing; Installation of utilities; Installation of flexible pavement; Installation of street light poles; Installation of traffic signals; Installation of signing and pavement markings; Installation of electrical duct bank; Relocation of over-height detection system; Installation of wireless vehicle detection system; Installation of landscape improvements; Installation of erosion and sediment control; Implementation of transportation management plan; Mobilization and demobilization, provision and maintenance of work and storage areas, Engineer's field facilities and performance of employee training; Removal and disposal of any material as a result of the activities listed above, unless stated otherwise in the contract drawings.

This project is 83.15% Federally Funded and 16.85% District-Funded. DDOT selected Capitol Paving of DC, Inc. (CPDC) as the contractor and awarded the \$12,055,691.00 contract on January 9, 2019. DDOT issued notice to proceed with contract work to CPDC with work to begin on 05/13/2019 and a substantial completion date of 11/23/2020.

## 2. STATUS OF CONSTRUCTION / PROGRESS SUMMARY

Work this week was performed during the day on Sunday, November 8<sup>th</sup>, 2020 thru Saturday, November 14<sup>th</sup>, 2020. Please see the details below.

- Along NJ Ave between N St. and K St.
  - 445.000 LF of Pipe Sewer TV Inspection was performed.
- Along NY Ave and NJ Ave intersection.
  - Furnished and installed, 6 - Green Arrow Led Module.
- Along NJ Ave between N St. and H St. (various locations)
  - Pipe Sewer TV Inspection was performed.
- Along NY Ave and NJ Ave intersection.
  - Removed, 11 - Traffic Signal Poles and Traffic Signal Equipment.
  - Removed, 1 - Traffic Signal Controller and Cabinet.

### 3. PHOTOS OF WORK PERFORMED THIS PERIOD



Picture No. 1: 11/09/2020 – Punch List walk through in progress along NJ Ave between H St. and N St. for sidewalk and granite curb (North View)



Picture No. 2: 11/09/2020 – Punch List walk through in progress along NJ Ave between H St. and N St. for sidewalk and granite curb (South View)





Picture No. 3 – 11/10/2020 – Jaxson Point crew working on the overhead sign structure along NY Ave and Kirby St.  
(West View)



Picture No. 4 – 11/10/2020 – Equipment for CCTV inspection for sewer inspections along NJ Ave





Picture No. 5 – 11/12/2020 – Checking MOT set up along NY Ave between M St. and Morgan St. (South View)



Picture No. 6 – 11/13/2020 – Temporary tape markings being placed along NY Ave and NJ Ave intersection (South View)





Picture No. 7 – 11/13/2020 – DDOT working on the traffic signals for the lane switch along NY Ave and NJ Ave intersection (West View)



Picture No. 8 – 11/05/2020 – Jaxon Point working on the traffic signals for the lane switch along NY Ave and NJ Ave intersection (South View)
